



Stellenbosch

UNIVERSITY
IYUNIVESITHI
UNIVERSITEIT


forward together
sonke siya phambili
saam vorentoe

CH05: PROJECT EXECUTION AND ROLLOUT


Ms Anthea Venter

Adapted from slides
prepared by

*John Nicholas and
Herman Steyn*



Systems Development Cycle or Project Life Cycle

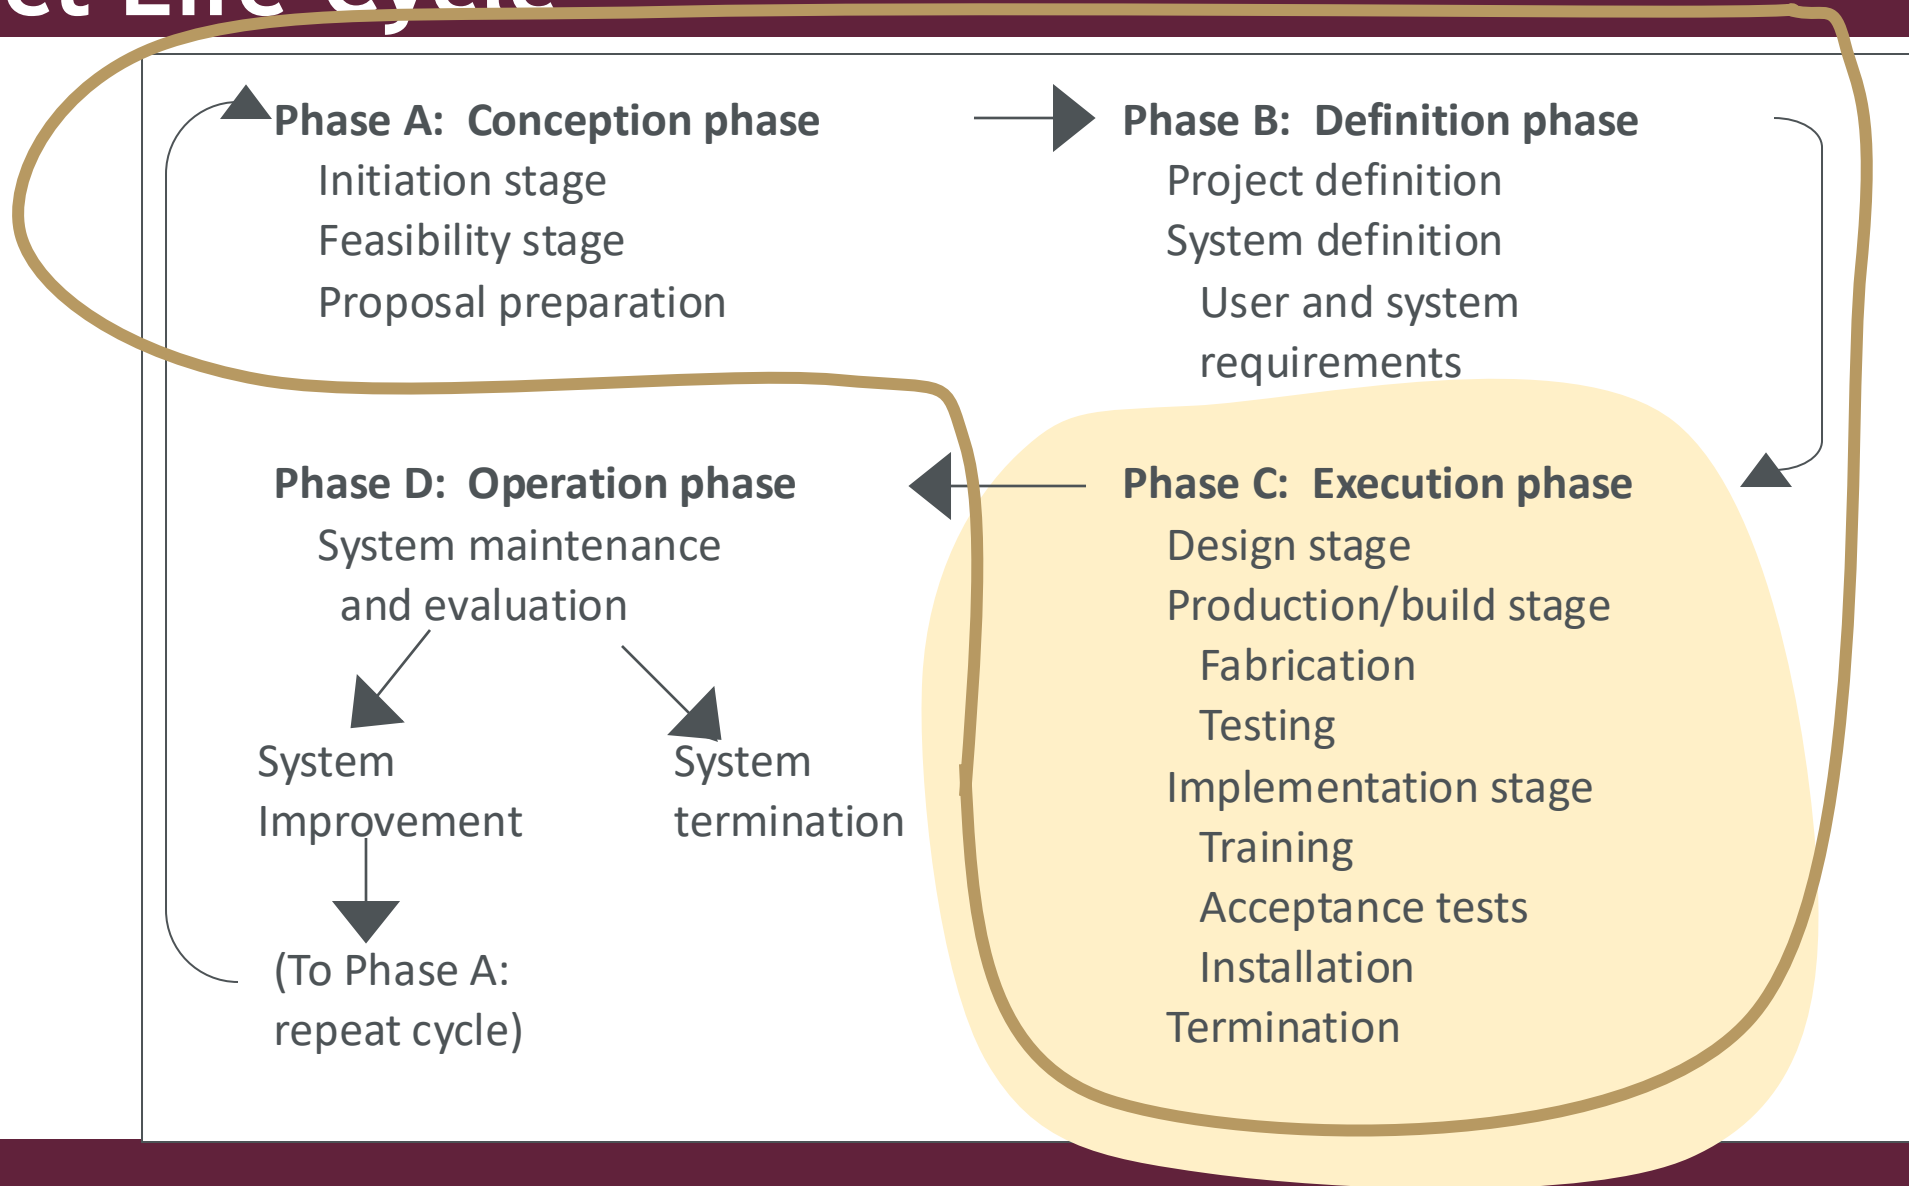


Phase C: Project Execution



- In addition to planning, scheduling, budgeting, and risk and quality management **responsibilities** already discussed, during Execution the PM is responsible for
 - Expanding the project team
 - Assigning responsibilities
 - Task integration
 - Documentation
 - Change control
 - Quality control
 - Production coordination
 - Inventory control
- When PM is not directly responsible for these, they **appoint** people who are


Detail Design Stage

- Design methodology: functional versus physical design
- Controlling design: Technical Review process
- Planning for production/build and later stages

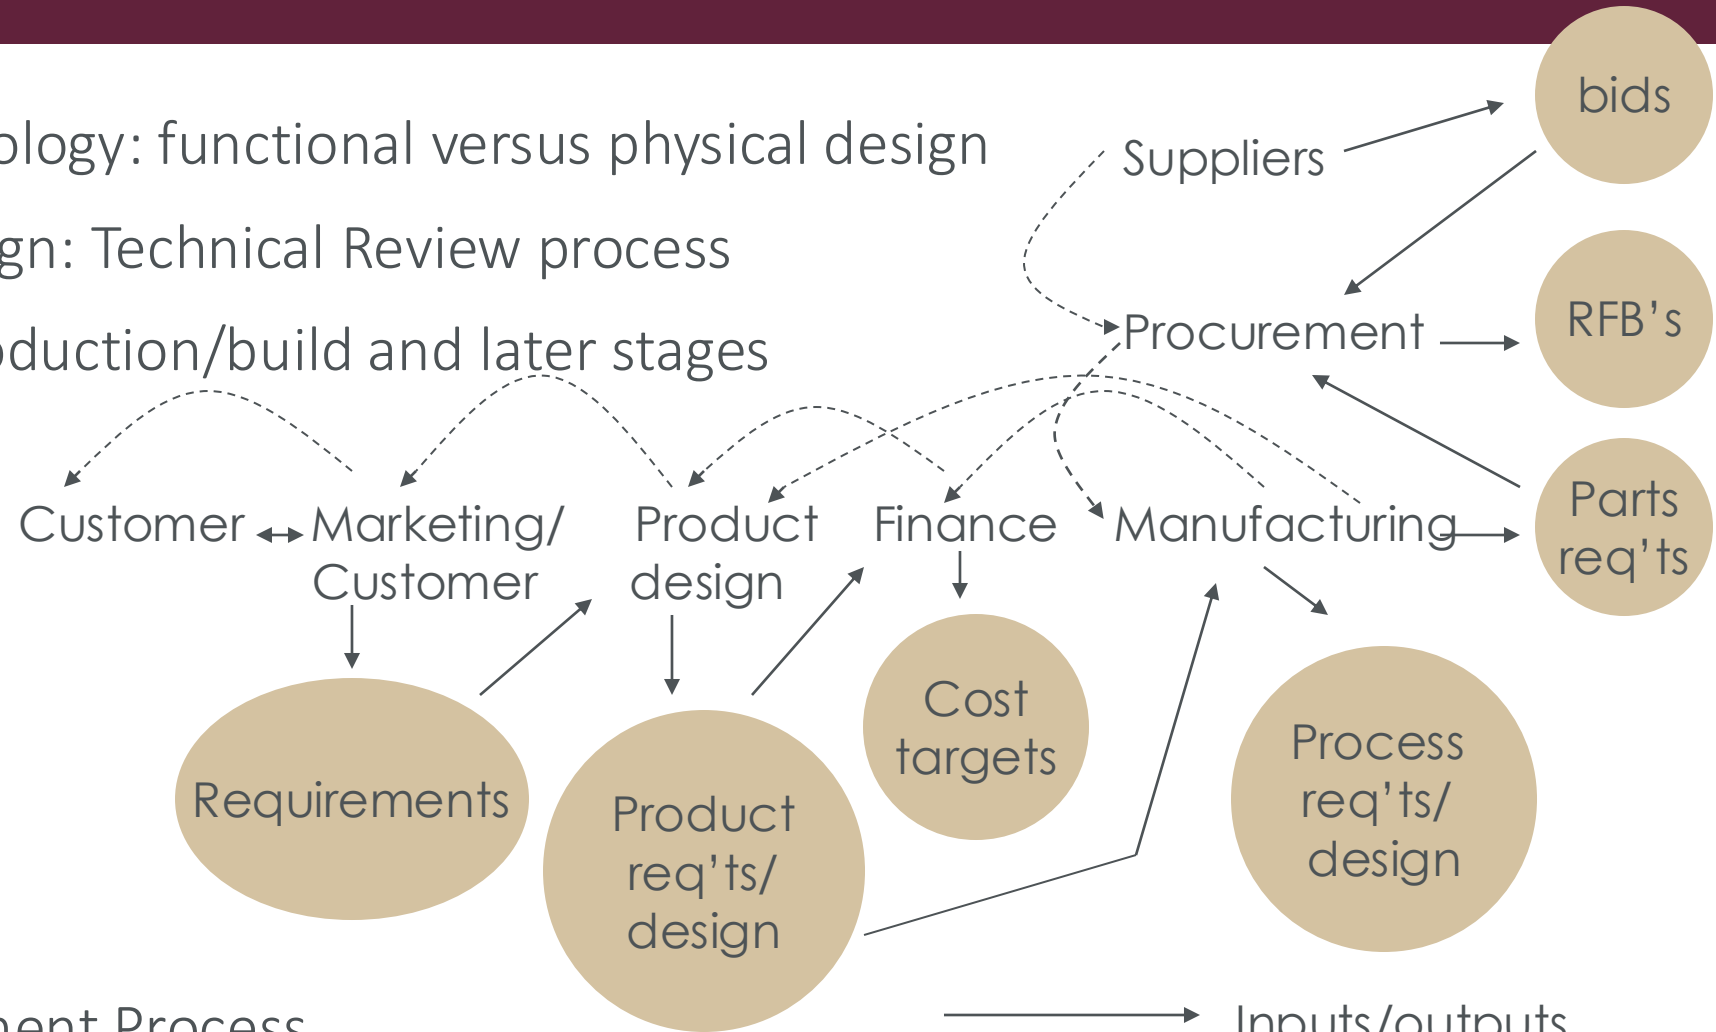

- Typical Development Process

Technical Review Process

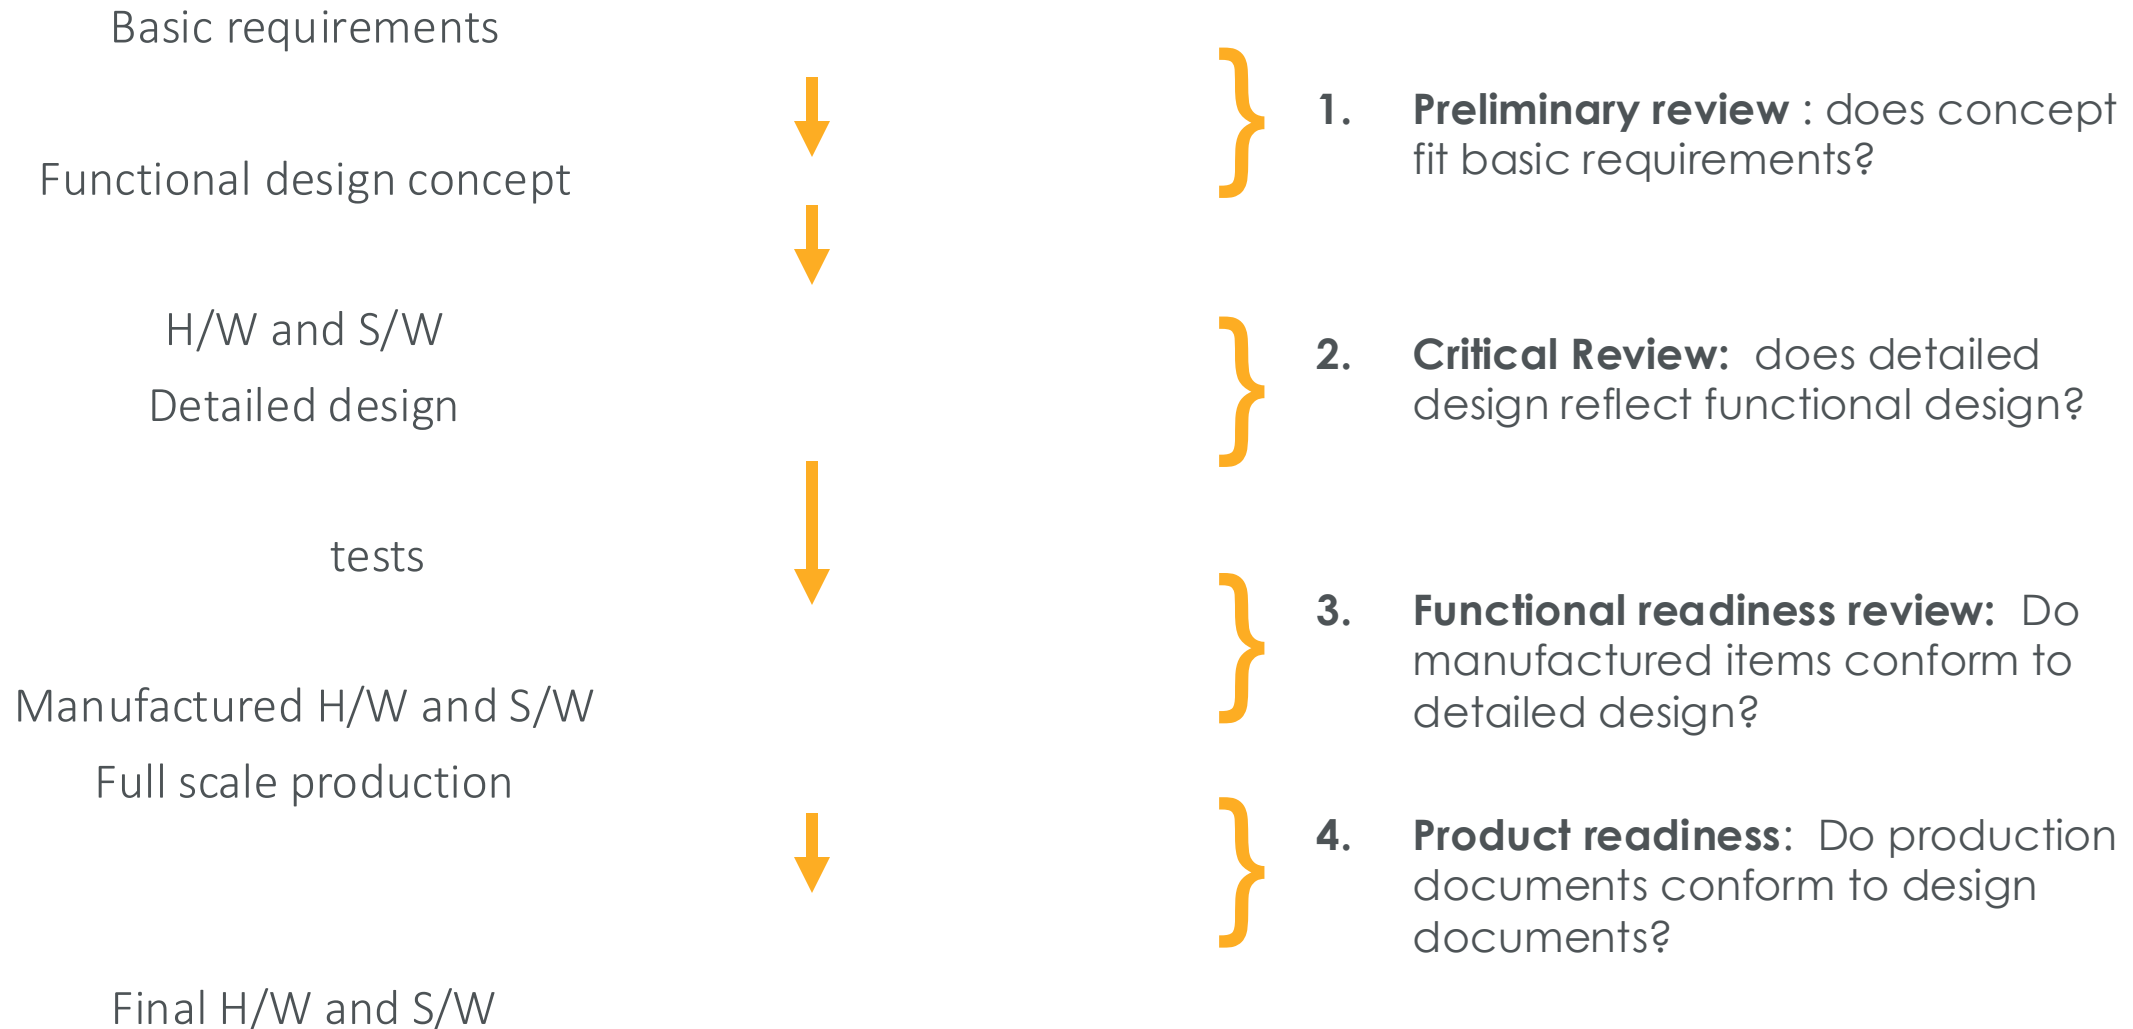


Production/Build Stage



- System fabrication/ construction/ assembly
- Testing: design vs. requirements vs. implementation
 - stress, failure, destructive vs. non-destruction (discussed in Chapter 10)
- Detailed planning for the implementation stage

Systems Development Cycle or Project Life Cycle

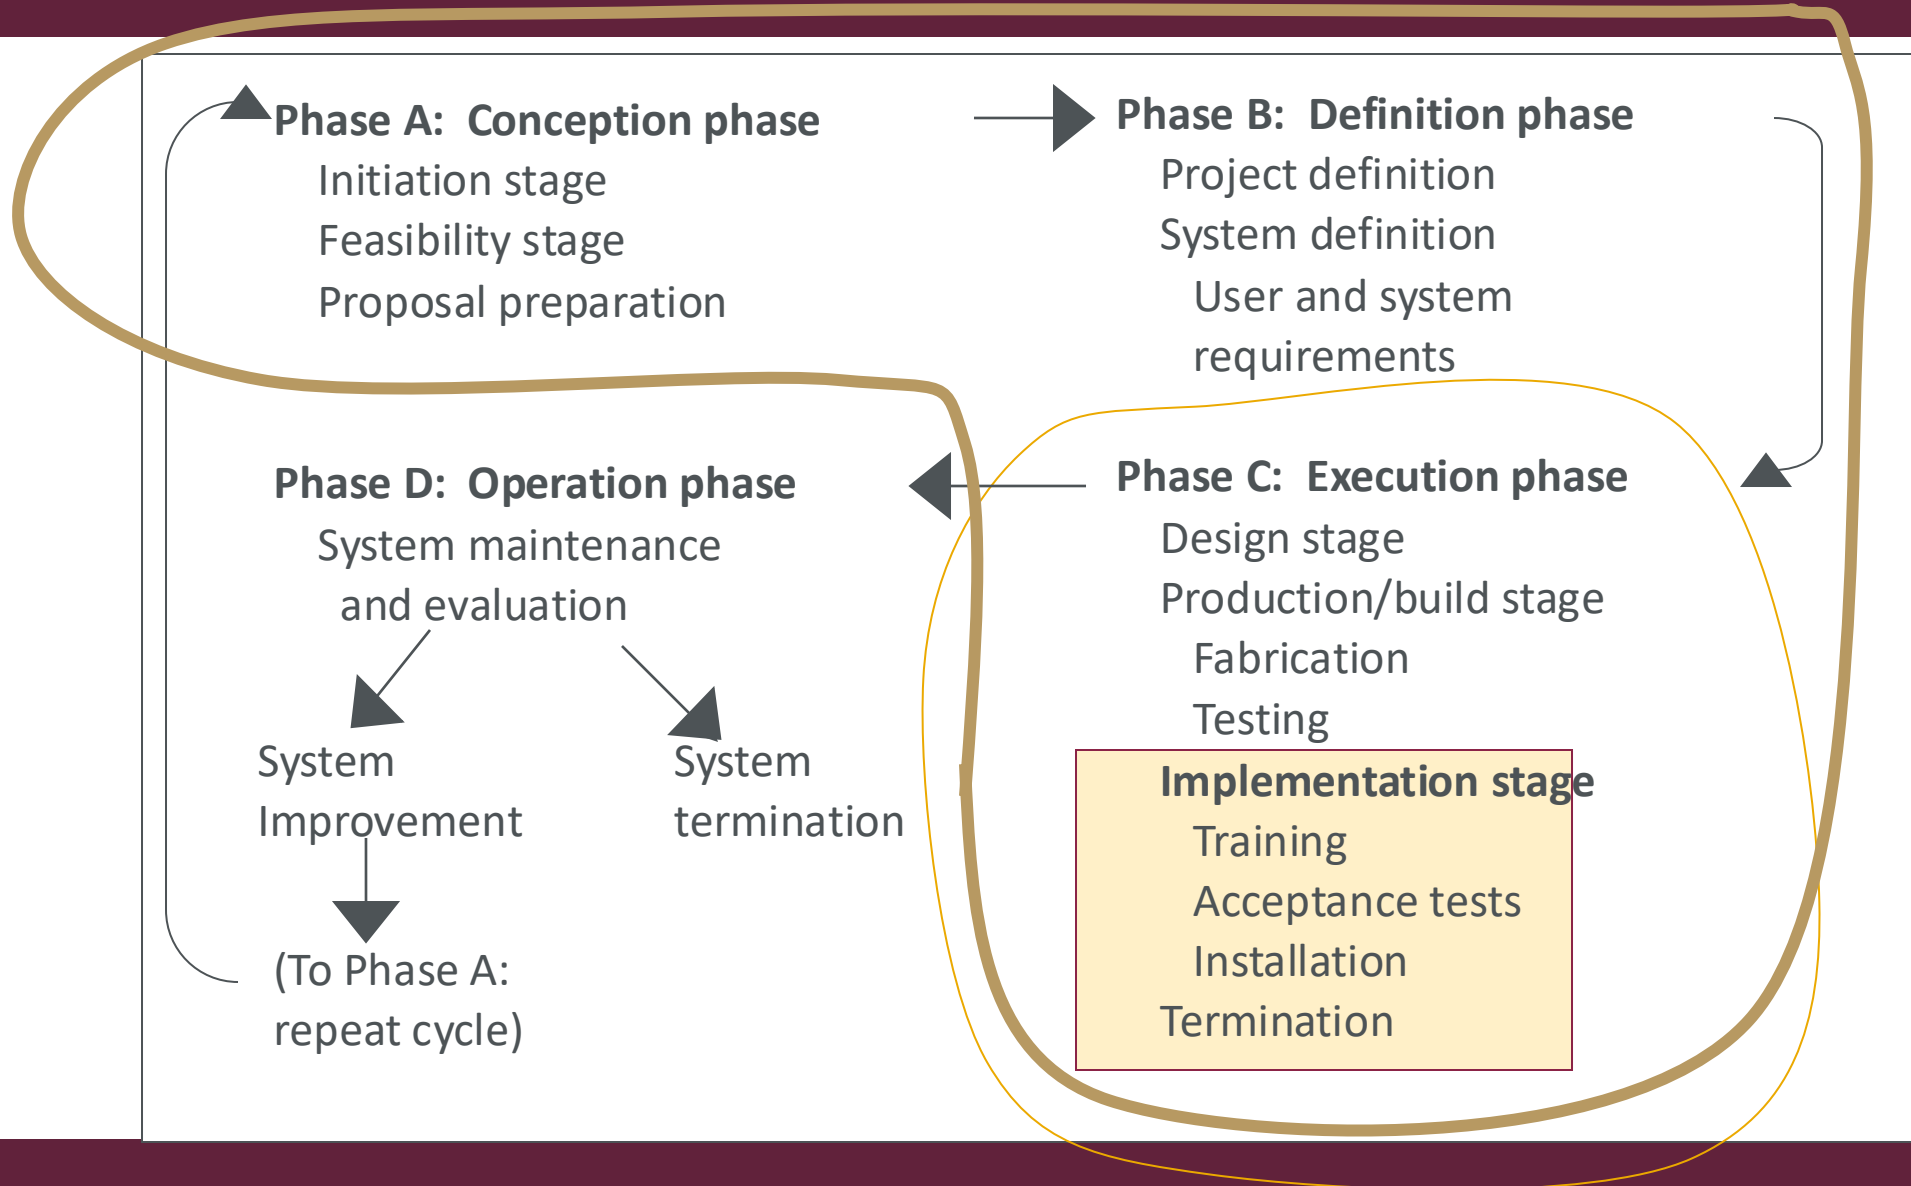


Implementation Stage



- User acceptance
 - User training
 - User acceptance testing
 - Modifications
 - Final user tests
- System installation and conversion process
 - Parallel, pilot, cold turkey
- User approval/punch list

Installation/ Conversion Strategies

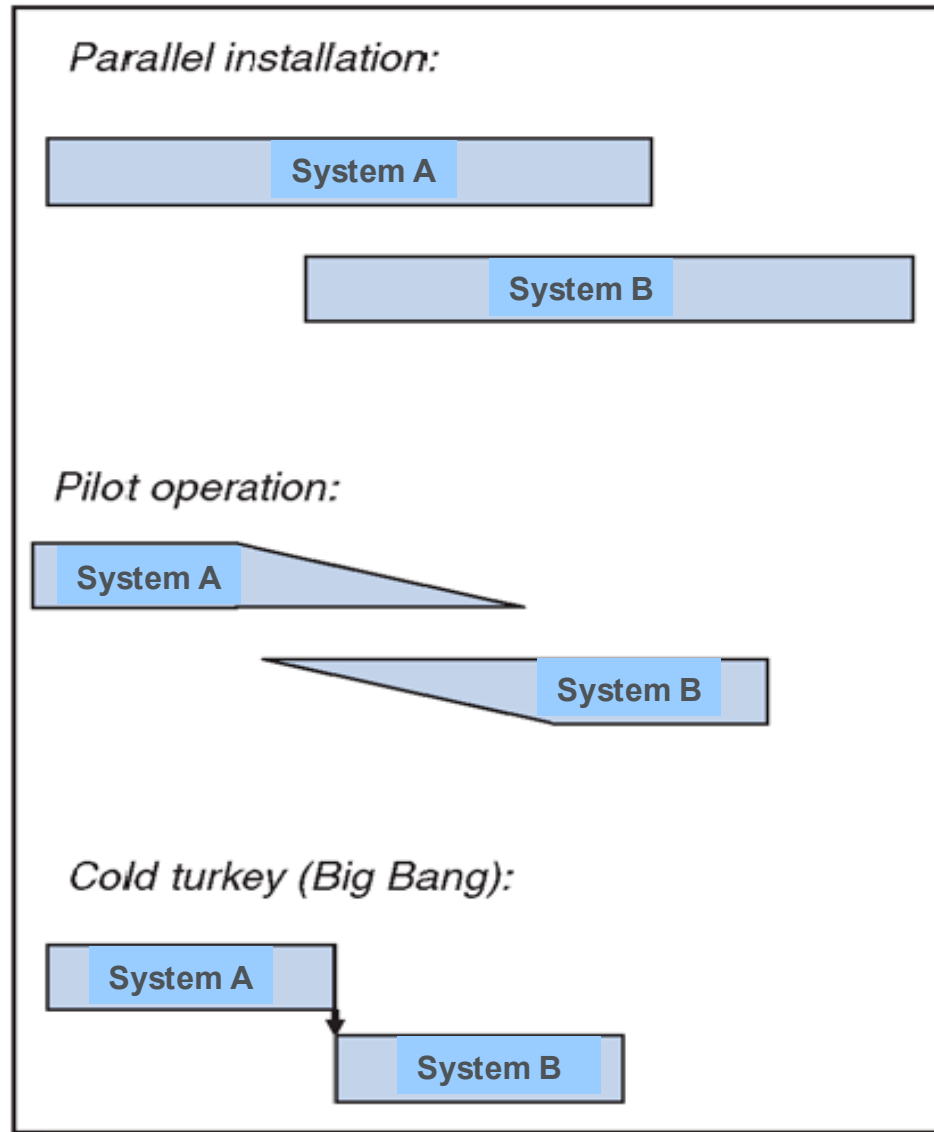


Stellenbosch

UNIVERSITY
IYUNIVESITHI
UNIVERSITEIT

forward together
sonke siya phambili
saam vorentoe

Systems Development Cycle or Project Life Cycle

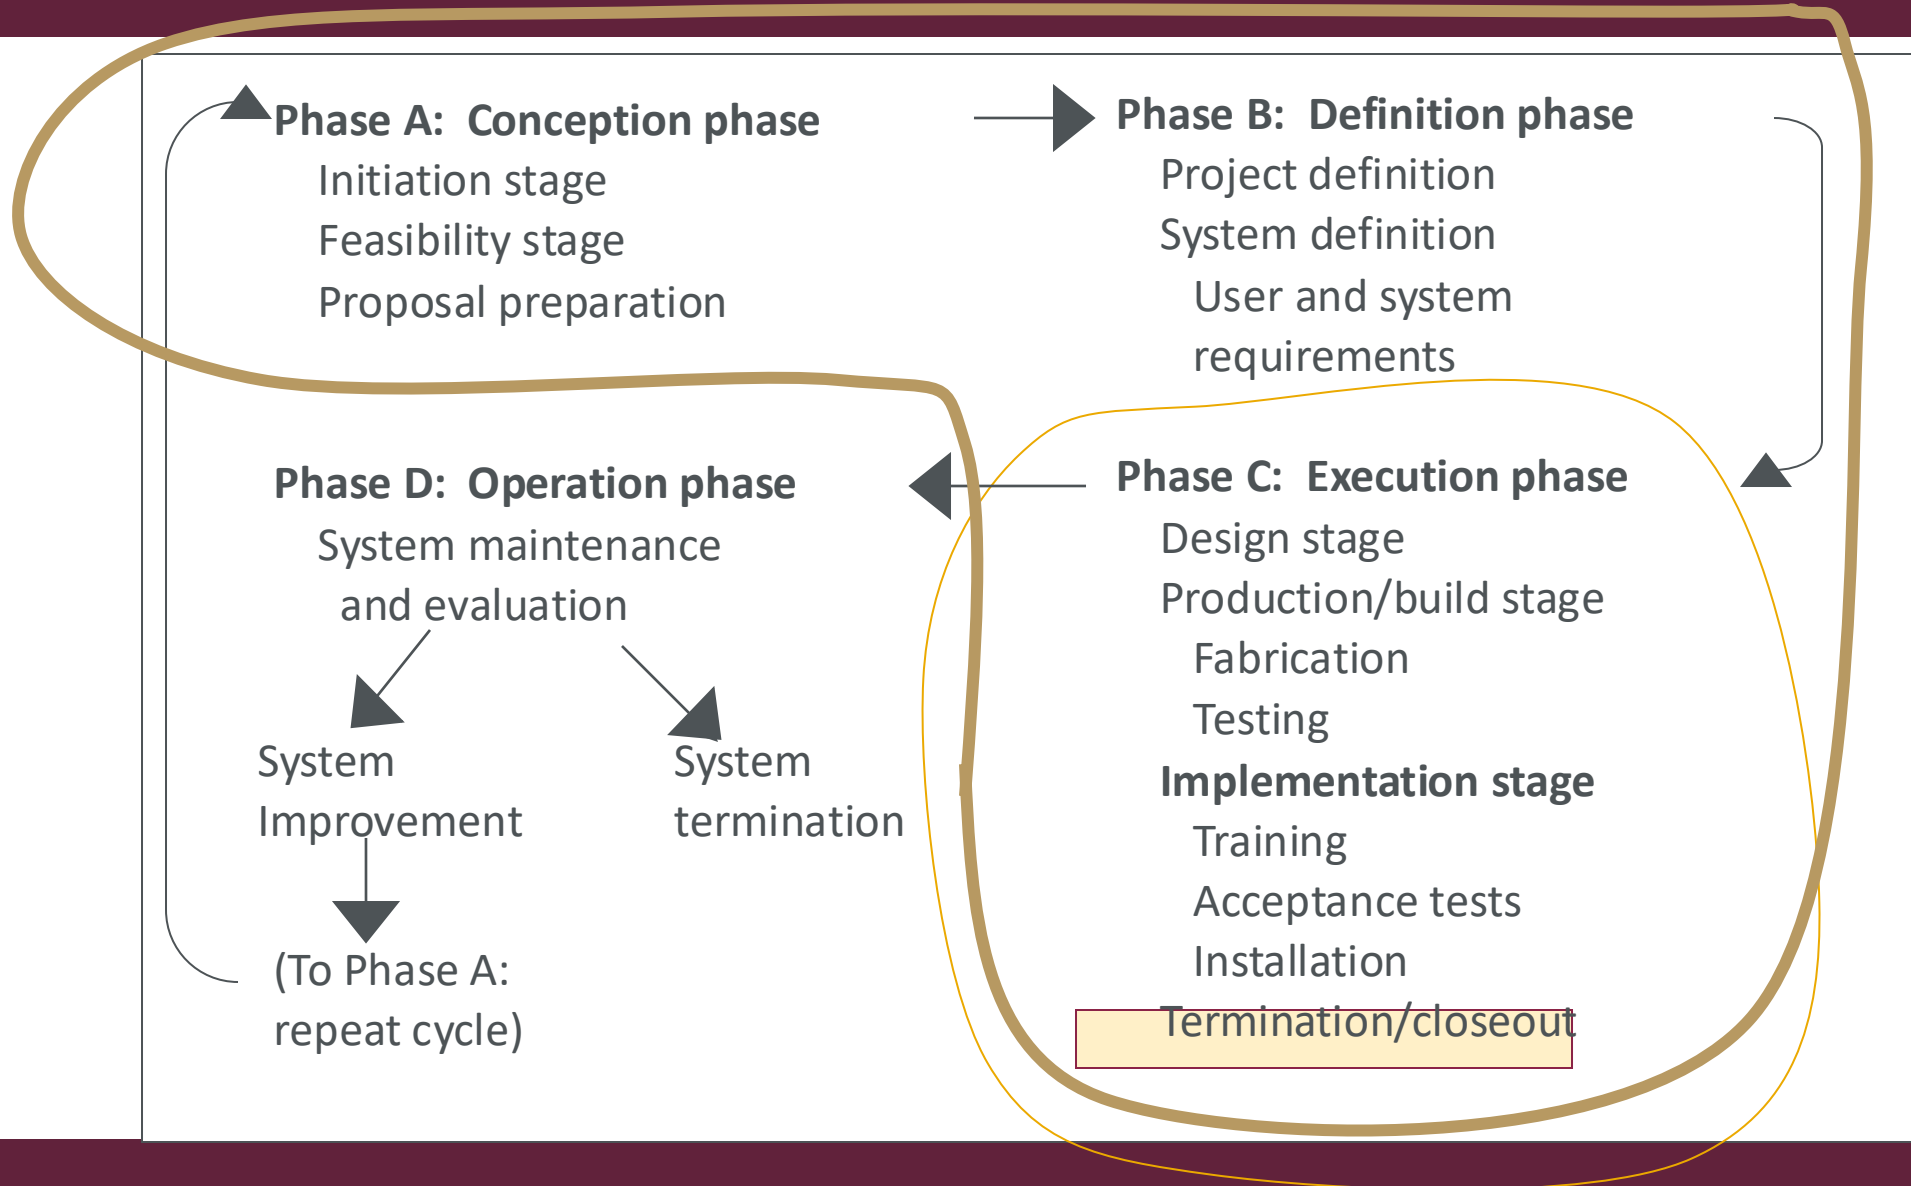

Termination and Close-out



- Termination
 - Planning, scheduling, monitoring of close-out
 - Final close-out
 - Customer acceptance, obligations, and payment activities
 - Post-completion project summary review/postmortem

Termination and Close-out Responsibilities



- Planning, scheduling, and monitoring completion activities:
 - Prepare and coordinate termination **plans and schedules**
 - Plan to reassign **project team** personnel, and transfer resources
 - **Monitor** termination activities and completion of all contractual agreements
 - Monitor **disposition** of surplus materials and special project equipment
- Final close-out activities:
 - Close out all work orders
 - Approve completion of all subcontracted work
 - Notify all departments and stakeholders of project completion
 - Close project office, project facilities, and project books
 - Close out contract, negotiate any adjustments

Project Summary Evaluation



Post-completion Project Review (Postmortem)

- Initial project performance, cost, and schedule objectives
- Soundness of objectives in view of initial problem or needs
- “Needs” that the end-item was supposed to fulfill
- Evolution of objectives; reasons for changes
- Project performance with respect to final objectives
- Effectiveness of project management; relationships among managers, project team members, subcontractors and suppliers, and customer
- Termination process: customer reactions and satisfaction


Project Summary Evaluation



Post-installation System Review

- Evaluates the fully operational end-item system
- Focuses on the end-item system
- Provides operation and maintenance information for the system's designers
- Addresses
 - Is the end-item doing what it was intended to do?
 - Is the user getting the expected benefits
 - What changes to the system would fulfill the user's needs?

Systems Development Cycle or Project Life Cycle

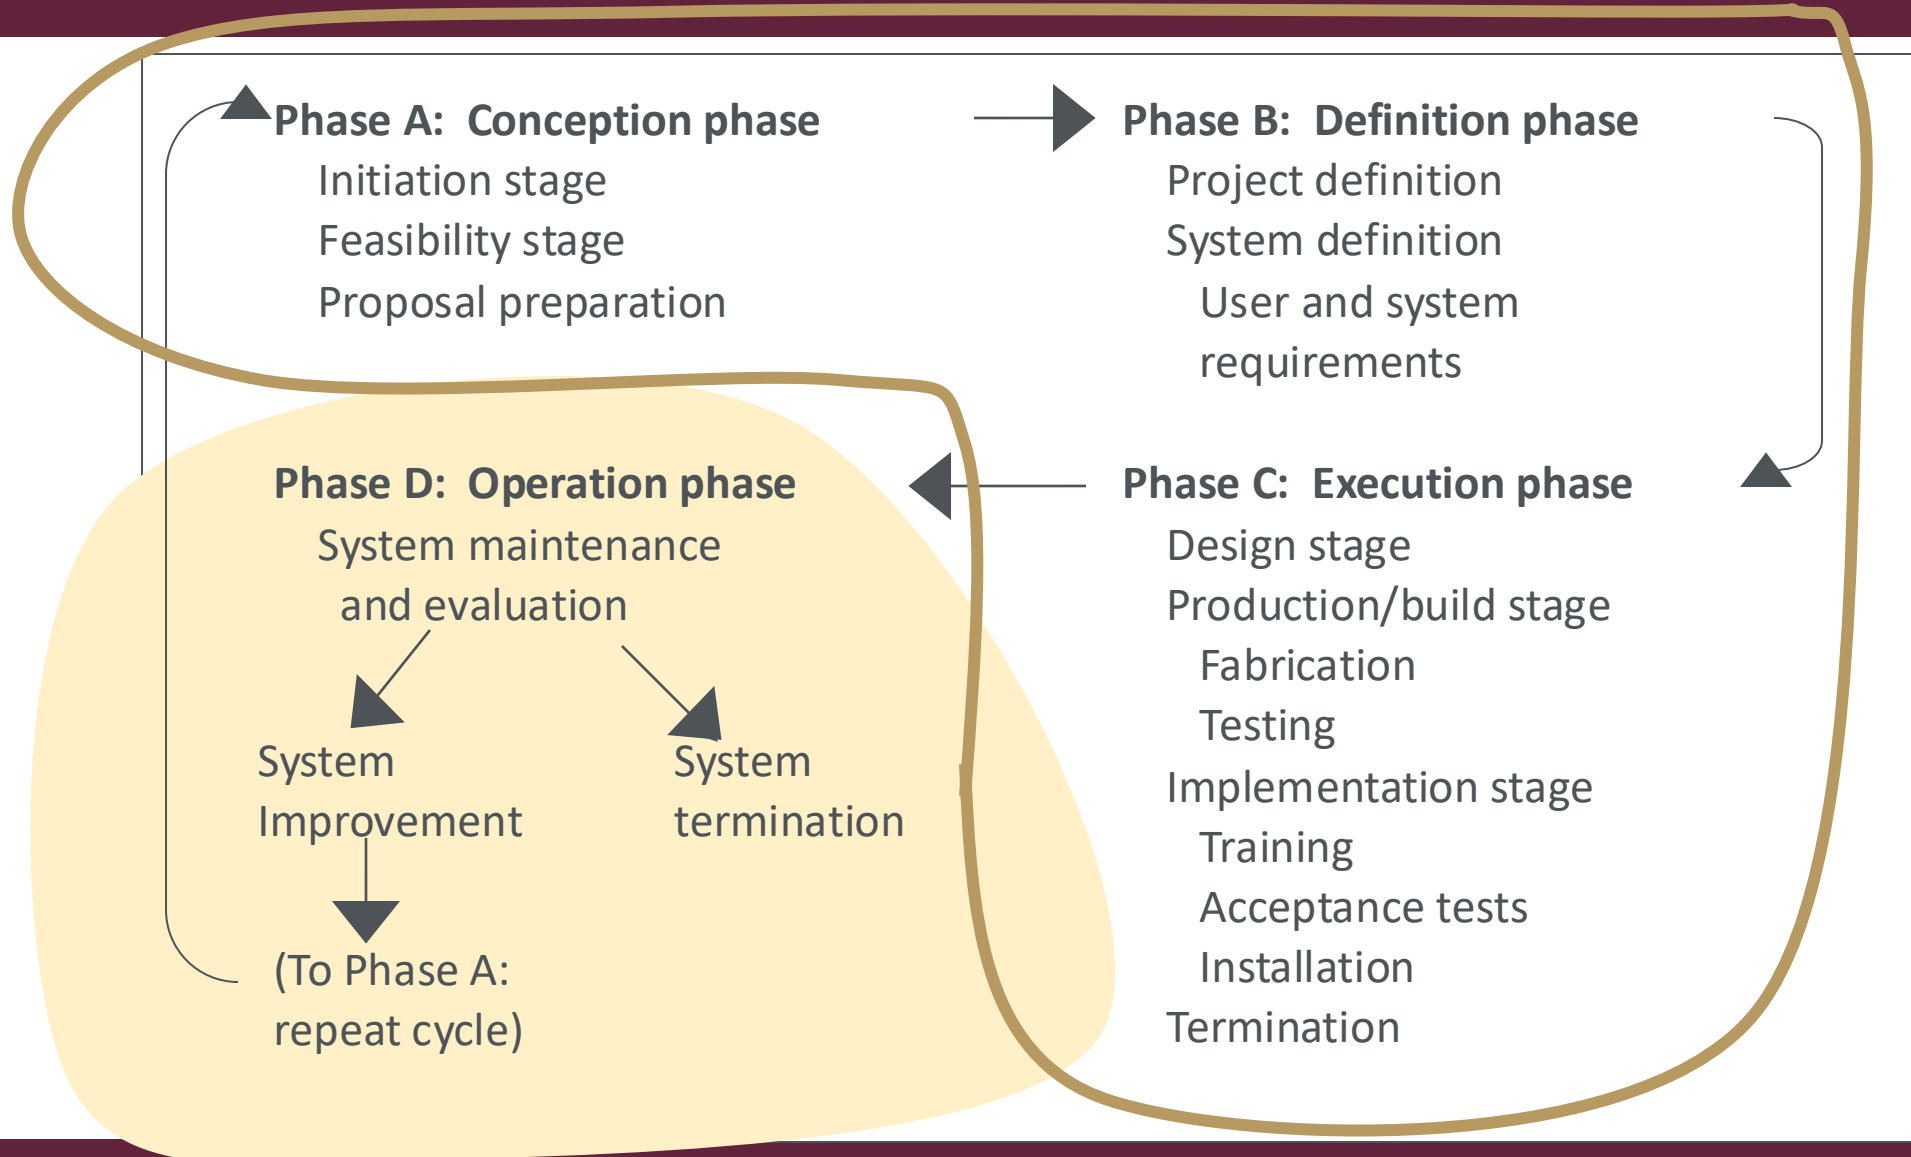

Phase D: Operation

- After completion of project and Phase C, project manager moves to other projects and core team disbands
- Sometimes, SDO remains involved with customer and end-item in some principal aspect of operation

Phase D: Operation



- System Evaluation and Maintenance
 - Repair/preventative maintenance /overhaul (MRO)
 - Standard, periodic maintenance
 - Post-installation review
- System Enhancement
 - Project extensions

Dark Side of Projects



- Like all human endeavors, projects sometimes include illegal or unethical practices. They include
 - Modern slavery
 - Corruption
 - Money laundering
 - Conflict of interest
 - Sexism and gender discrimination
 - Greenwashing
 - and there are more!
- The hope is that project managers can resist these practices or ameliorate their consequences whenever possible.

Thank you
Enkosi
Dankie

